USMC Fielding Plan

Draft USMC Fielding Plan

The Future of Towed Cannon Artillery

	FY05	
2	JAN 05	APG OPTICAL & ARTILLERY REPAIR
8	JAN 05	FORT SILL NETT
18	APR 05	11th MARINES – 29 PALMS
18	JUN 05	11th MARINES – CAMP PENDLETON
1	AUG 05	APG OPTICAL & ARTILLERY REPAIR
18	SEPT 05	11th MARINES – CAMP PENDLETON
	FY06	
18	JAN 06	EAPP 29 PALMS
18	MAY 06	10th MARINES – CAMP LEJEUNE
18	JUN 06	10th MARINES – CAMP LEJEUNE
18	AUG 06	10th MARINES – CAMP LEJEUNE
		–
	FY07	
18	SEP 06	10th MARINES – CAMP LEJEUNE
	MAR 07	12th MARINES – HAWAII
24	JUN 07	12th MARINES
6	JUL 07	EEAP – CAMP FUJI
	FY08	
14	NOV 07	DEPOT MAINTENANCE FLOAT
18	JUL 08	14th MARINES
18	AUG 08	14th MARINES
	FY09	
18	AUG 09	14th MARINES
18	SEP 08	14th MARINES

Test Sites

1	**Feb 06**	**Picatinny**
1	**Apr 06**	**YPG**
1	**May 06**	**Aberdeen**
1	**Jul 06**	**Ft. Greely**
1	**Sep 06**	**Tropic Test Ctr**
1	**Nov 06**	**WSMR**
1	**Feb 07**	**Dugway**

MPS SHIP FIELDING PLAN

MPS I – CAMP LeJEUNE		
8	APR 07	BLOUNT ISLAND
7	JUN 07	BLOUNT ISLAND
8	AUG 07	BLOUNT ISLAND
7	OCT 07	BLOUNT ISLAND
MPS II – CAMP PENDLETON		
6	APR 08	BLOUNT ISLAND
6	MAY 08	BLOUNT ISLAND
6	JUL 08	BLOUNT ISLAND
6	OCT 08	BLOUNT ISLAND
6	NOV 09	BLOUNT ISLAND
MPS III – OKINAWA		
9	DEC 08	BLOUNT ISLAND
6	JUL 09	BLOUNT ISLAND
9	SEP 09	BLOUNT ISLAND
6	NOV 09	BLOUNT ISLAND

Draft Fielding Plan (AAO)

The Future of Towed Cannon Artillery

FY 05			FY 06				FY 07				FY 08				FY 09				
2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1

11th Marines (72)

10th Marines (72)

12th Marines (36)

14th Marines (54)

MPS I (30)

MPS II (30)

MPS III (30)

Fort Sill (8) APG (2)

APG (1)

EEAP 29 Palms (18)

DMF (14)

EEAP Camp Fuji (6)

Test Centers (6)

Draft Fielding Plan w/ HIMARs

The Future of Towed Cannon Artillery

FY 05			FY 06				FY 07				FY 08				FY 09				
2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1

11th Marines (72)

(-18) 5/11 HIMARS

10th Marines (72)

12th Marines (36)

14th Marines (54) (+18) 1 BN VICE 2 HIMARS

MPS I (30)

MPS II (30)

MPS III (30)

Fort Sill (8) APG (2)

APG (1)

EEAP 29 Palms (18)

DMF (14)

EEAP Camp Fuji (6)

Test Centers (6)

New Equipment Trainin

Marine NET Team (M777)

The Future of Towed Cannon Artillery

Officer in Charge (JPMO Billet)	Major	MOS 0802
Assistant OIC	CWO4	MOS 2120 (JPMO Billet)
6 Operator Instructors	SSgt / Civilian	MOS 0811 / 13B
2 Maintenance Instructors	SSgt / Sgt	MOS 2131 / 2171
2 Equipment Specialists	Civilian	
Fire Control Specialist	Civilian	

* NETT under the command of the JPM

Operator NET

The Future of Towed Cannon Artillery

O-NET

Train Section Chiefs
18 –Sec Chiefs/ Battalion
6 - Trainers

A Bty
54 – 0811's
6 –Sec Chiefs
2 - Trainers

B BTY
54 – 0811's
6 –Sec Chiefs
2 - Trainers

C BTY
54 – 0811's
6 –Sec Chiefs
2 - Trainers

LRIP FIELDINGS
Basic Gun – M777
18 Howitzers
Per Battalion

Target Audience
Instructors

Maintenance NET

The Future of Towed Cannon Artillery

M - NET

7 – 2131's 2nd ECH

6 – 2131's 3rd/4th ECH

2 - Trainers

6 – 2171's 3rd/4th ECH

1 - Trainer

M777 NET

The Future of Towed Cannon Artillery

	Week 1	Week 2	Week 3	Week 4	Week 5
Maintainer **2 Maintainer Trainers**	 6 MOS 2131  7 MOS 2131	 6 MOS 2131  7 MOS 2131	 6 MOS 2131 5 MOS 2171  7 MOS 2131		
Operator **6 Operator Trainers**			 4 MOS 0802 4 MOS 0811  4 MOS 0802 21 MOS 0811 **HHQ and SC**	 180 MOS 0811 **Section Tng**	 180 MOS 0811 **Live Fire**

M777E1 NET

The Future of Towed Cannon

	Week 1	Week 2	Week 3	Week 4	Week 5	Week 6
Maintainer **3 Maintainer Trainers**	 6 MOS 2131  7 MOS 2131 3 MOS 2887 (RGT)	 6 MOS 2131  7 MOS 2131 3 MOS 2887 (RGT)	 6 MOS 2131  7 MOS 2131 3 MOS 2887 (RGT)	 6 MOS 2131 5 MOS 2171  7 MOS 2131		
Operator **6 Operator Trainers**			 4 MOS 0802 4 MOS 0811  4 MOS 0802 21 MOS 0811 **TTP**	 4 MOS 0802 4 MOS 0811  4 MOS 0802 21 MOS 0811 **HHQ and SC**	 180 MOS 0811 **Section Tng**	 180 MOS 0811 **Live Fire**

Timeline

The Future of Towed Cannon Artillery

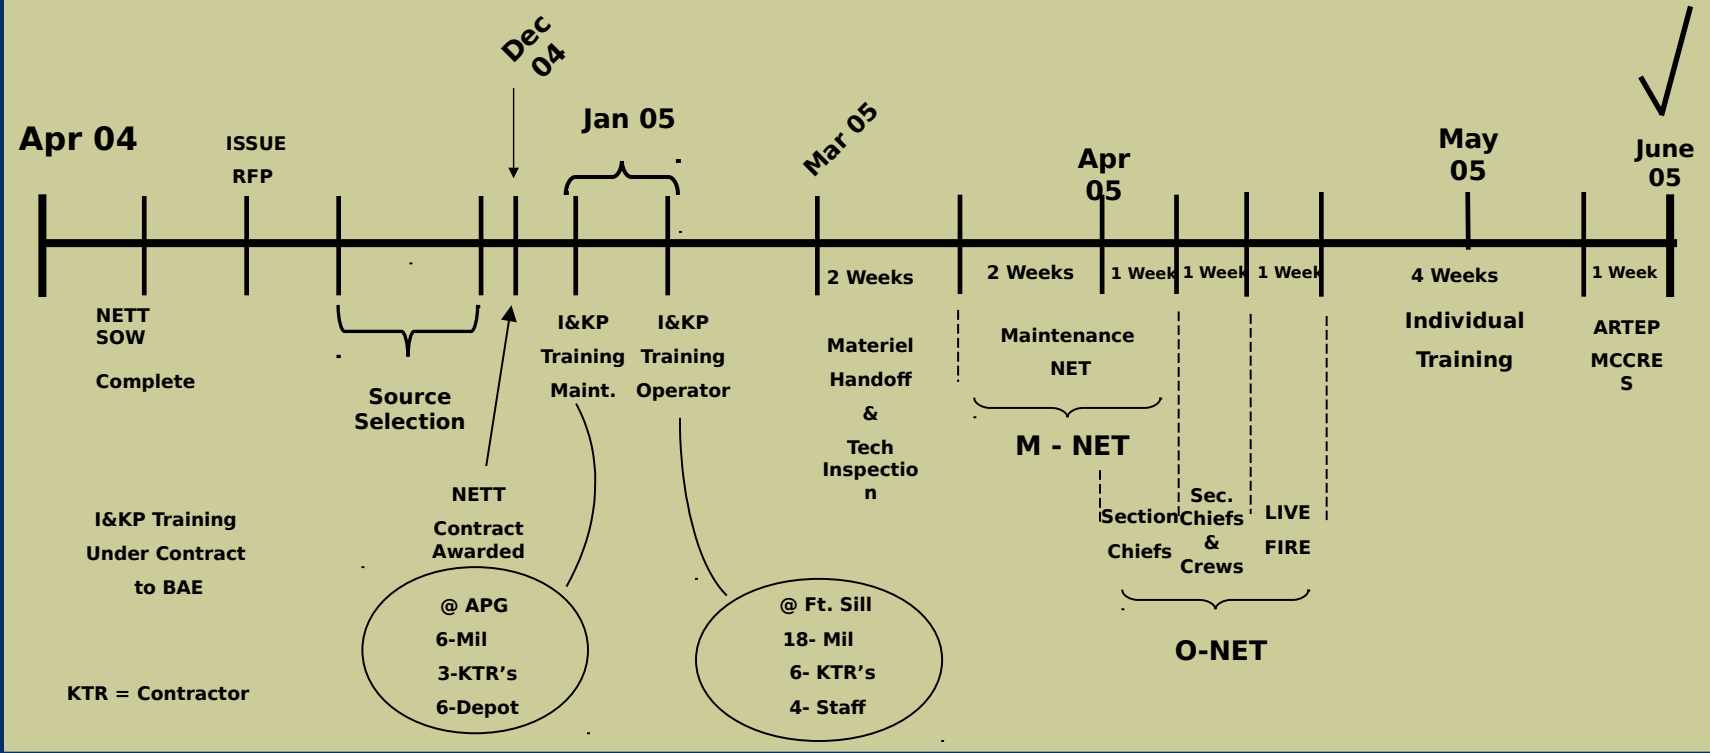

Active vs. Reserve Fielding - Operator

The Future of Towed Cannon Artillery

ACTIVE

	Wk 1	Wk 2	Wk 3	Wk 4
HQ	4 MOS 0802 / 4 MOS 0811		180 MOS 0811	
Btry	4 MOS 0802 TTP	21 MOS 0811 HHQ & SC	Section Tng	Live Fire

RESERVE

Ft. Sill		Assistance Visits		AT Period	
Wk 1	Wk 2	Weekend 1	Weekend 2	Wk 3	Wk 4
6 Btry Gunnies / I&I AD		33 MOS 0802 & 0811 SMCR	33 MOS 0802 & 0811 SMCR	180 MOS 0811 SMCR	
Train the Trainer		TTP	HHQ & SC	Section Tng	Live Fire

14th Marines O-NET Assumptions

The Future of Towed Cannon Artillery

- **Field max 2 Battalions per year due to CAX Requirements, will take 2 years to field 14th Marine Regiment**
- **All AD Battery and I&I Officers travel to Ft. Sill for O-NET and will support O-NETT with designated Unit Training Requirements**
- **Artillery Battalion Personnel trained through 2 weekend Assistance Visits and during 2 week AT**

Active vs. Reserve - Maintainer

The Future of Towed Cannon Artillery

ACTIVE

Wk 1 | Wk 2 | Wk 3 | Wk 4

13 MOS 2131

3 MOS 2887 | 6 MOS 2171

RESERVE

APG

Wk 1 | Wk 2 | Wk 3 | Wk 4

7 MOS 2131 AD

2 MOS 2887 AD | 4 MOS 2171 AD

Train the Trainer

Unit Training During Weekend Drills

AT Period

Wk 1 | Wk 2

6 MOS 2131 SMCR

12 MOS 2887 SMCR

6 MOS 2171 SMCR

M-NETT

Intensive Train Up

AT Support Provided By:

- AD Maintainers
- M-NETT Instructors

M777E1 M-NET Assumptions

The Future of Towed Cannon Artillery

- **Field max 2 Battalions per year due to CAX Requirements, will take 2 years to field 14th Marine Regiment**
- **All AD Students travel to APG for M-NET**
- **AD Students Cluster Trained**
- **SMCR Students trained through Train the Trainer Method and Supplemental Training during 2 week AT**
- **AD maintainers to provide Maintenance Support**

14th Marines NET Summary

The Future of Towed Cannon Artillery

- **Reserve Units will receive same training as Active Units**
- **Training will be structured to meet Reserve Units availability**
- **Training will maximize utilization of assigned Active Duty Personnel**
- **Reserve Unit Fieldings will be limited to 2 Battalions per year**
